Interreg NEXT Romania – Ukraine

Co-funded by the European Union

Stefan cel Mare University of Suceava

Ivano-Frankivsk National Technical University of Oil and Gas

LIFECED

LIFELONG AND CULTURAL INCLUSIVE EDUCATION ON THE ROMANIAN-UKRAINIAN BORDER

Training: PROJECT MANAGEMENT

cod ROUA00256

www.ro-ua.net

Interreg NEXT Romania – Ukraine

Co-funded by the European Union

Stefan cel Mare University of Suceava

Ivano-Frankivsk National Technical University of Oil and Gas

Project management

Module 4. Project logic, results, indicators & logical framework thinking

LIFECED Project

Interreg NEXT Romania – Ukraine
Co-funded by the European Union

Stefan cel Mare University of Suceava

Ivano-Frankivsk National Technical University of Oil and Gas



The Intervention Logic

Each operational level directly unlocks and substantiates the next tier of project success

Inputs & Activities

Grant funding, consortium partner person-months, and operational work packages executed during the grant period.

Outputs

Concrete tangibles and deliverables produced directly under project control (such as toolkits, prototypes, and technical reports).

Outcomes (Results)

Medium-term effects and institutional uptake observed among target beneficiaries during and right after the project.

Impact

Broader, systemic socioeconomic, scientific, or policy benefits sustained long after the grant agreement concludes.

Made with Napkin

Interreg Co-funded by the European Union
NEXT Romania – Ukraine



Stefan cel Mare University of Suceava

Ivano-Frankivsk National Technical University of Oil and Gas

Structure of the Logical Frame Matrix

Project title: _____ Target group: _____ Version:

Target area: _____ Project period: _____ Date:_____

Narrative summary	Indicators	Means of Verification	Hypotheses
General objective			
Purpose project			
Results			
Activities	**Inputs** - Experts - Facilities and equipment - Budget - Other required inputs		**Pre-Conditions**


Project summary

General purpose
Goods and/or conditions that are produced directly from the project

Purpose of the project
Objectives expected to be achieved through Project fulfillment

Project results
The development effects expected by achieving the purpose of the project


Project activities
Series of specific actions required for production of results

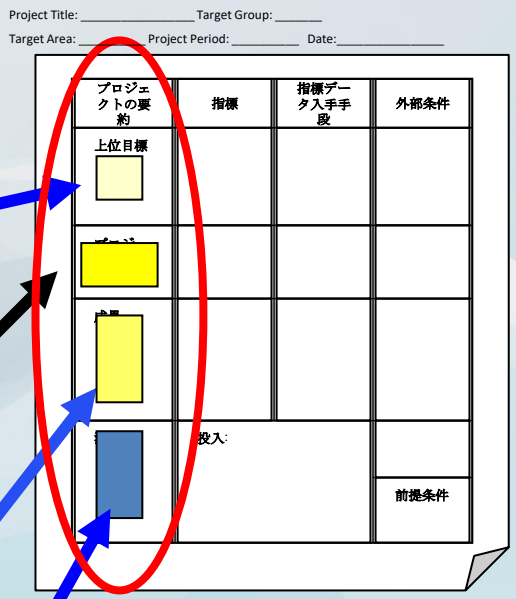

Outputs vs Results

The Critical Distinction

Delivering an output does not guarantee a result: publishing an open-access toolkit is an output, whereas 40 regional hospitals integrating it into diagnostic workflows is a result.

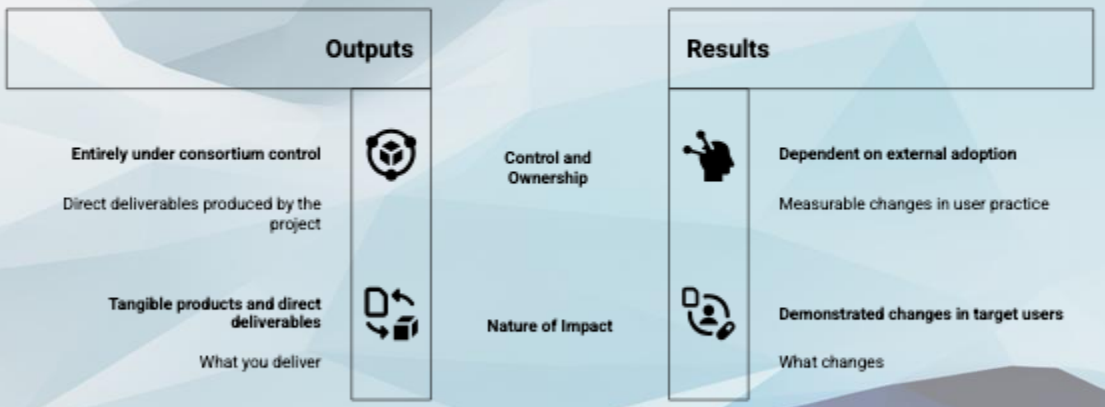

Made with Napkin

Practical KPI Examples and Indicators



Output KPI

Deliver 6 specialized SME webinars reaching 300 participants across 8 EU member states. Verification: Signed participant logs, webinar recordings, and attendee completion certificates.

1



Outcome KPI

At least 40% of participating SMEs implement the digital security protocol within 6 months of training (Baseline: 5%). Verification: Follow-up operational audit surveys and self-assessment logs.

2



Impact KPI

Achieve a 25% reduction in incident response times across adopting regional networks 2 years post-project. Verification: Published regional agency reports and independent sector evaluations.

3

Made with Napkin

Action plan

The action plan shows in great detail how the objectives will be met, clearly stating:

- **Detailed activities and the correlation between them**
- **Responsibilities**
- **Deadlines**
- **Resources**
- **Standards, criteria and indicators for measuring results**
- **Risks and obstacles (personal or environmental)**

Pre-proposal of the project

1. Title:
2. Acronym:
3. Project description (Purpose):
4. Target groups:
5. Duration (period):
6. Consortium (partners):
7. Objectives:
8. - Main Objective
9. - Specific Objectives (Intermediate) / Work Packages
10. - Activities (durations, interdependencies, resources)
11. Budget:
12. Funders:
13. Appendices (SWOT Analysis, Gantt Chart, Logical Framework Matrix)

Interreg Co-funded by the European Union
NEXT Romania – Ukraine

Stefan cel Mare University of Suceava

Ivano-Frankivsk National Technical University of Oil and Gas

➡️ EU grant: 276.107,50 Euro

The Interreg VI-A NEXT Romania-Ukraine Programme 2021- 2027 is financed by the European Union and co-financed by the participating countries in the Programme.

This material has been produced with the assistance of the European Union. The contents of this material are the sole responsibility of Stefan cel Mare University of Suceavaand can in no way be taken to reflect the views of the European Union or of the Interreg VI-A NEXT Romania-Ukraine Programme 2021- 2027 management structures

Contact
✉️ Email: lifeced@usm.ro
https://lifeced.usv.ro/ro_ro/
